




Caltrans District 4 Active Projects in Napa County

September 2025

September 22, 2025
ATAC Item 6.5
Continued From: New

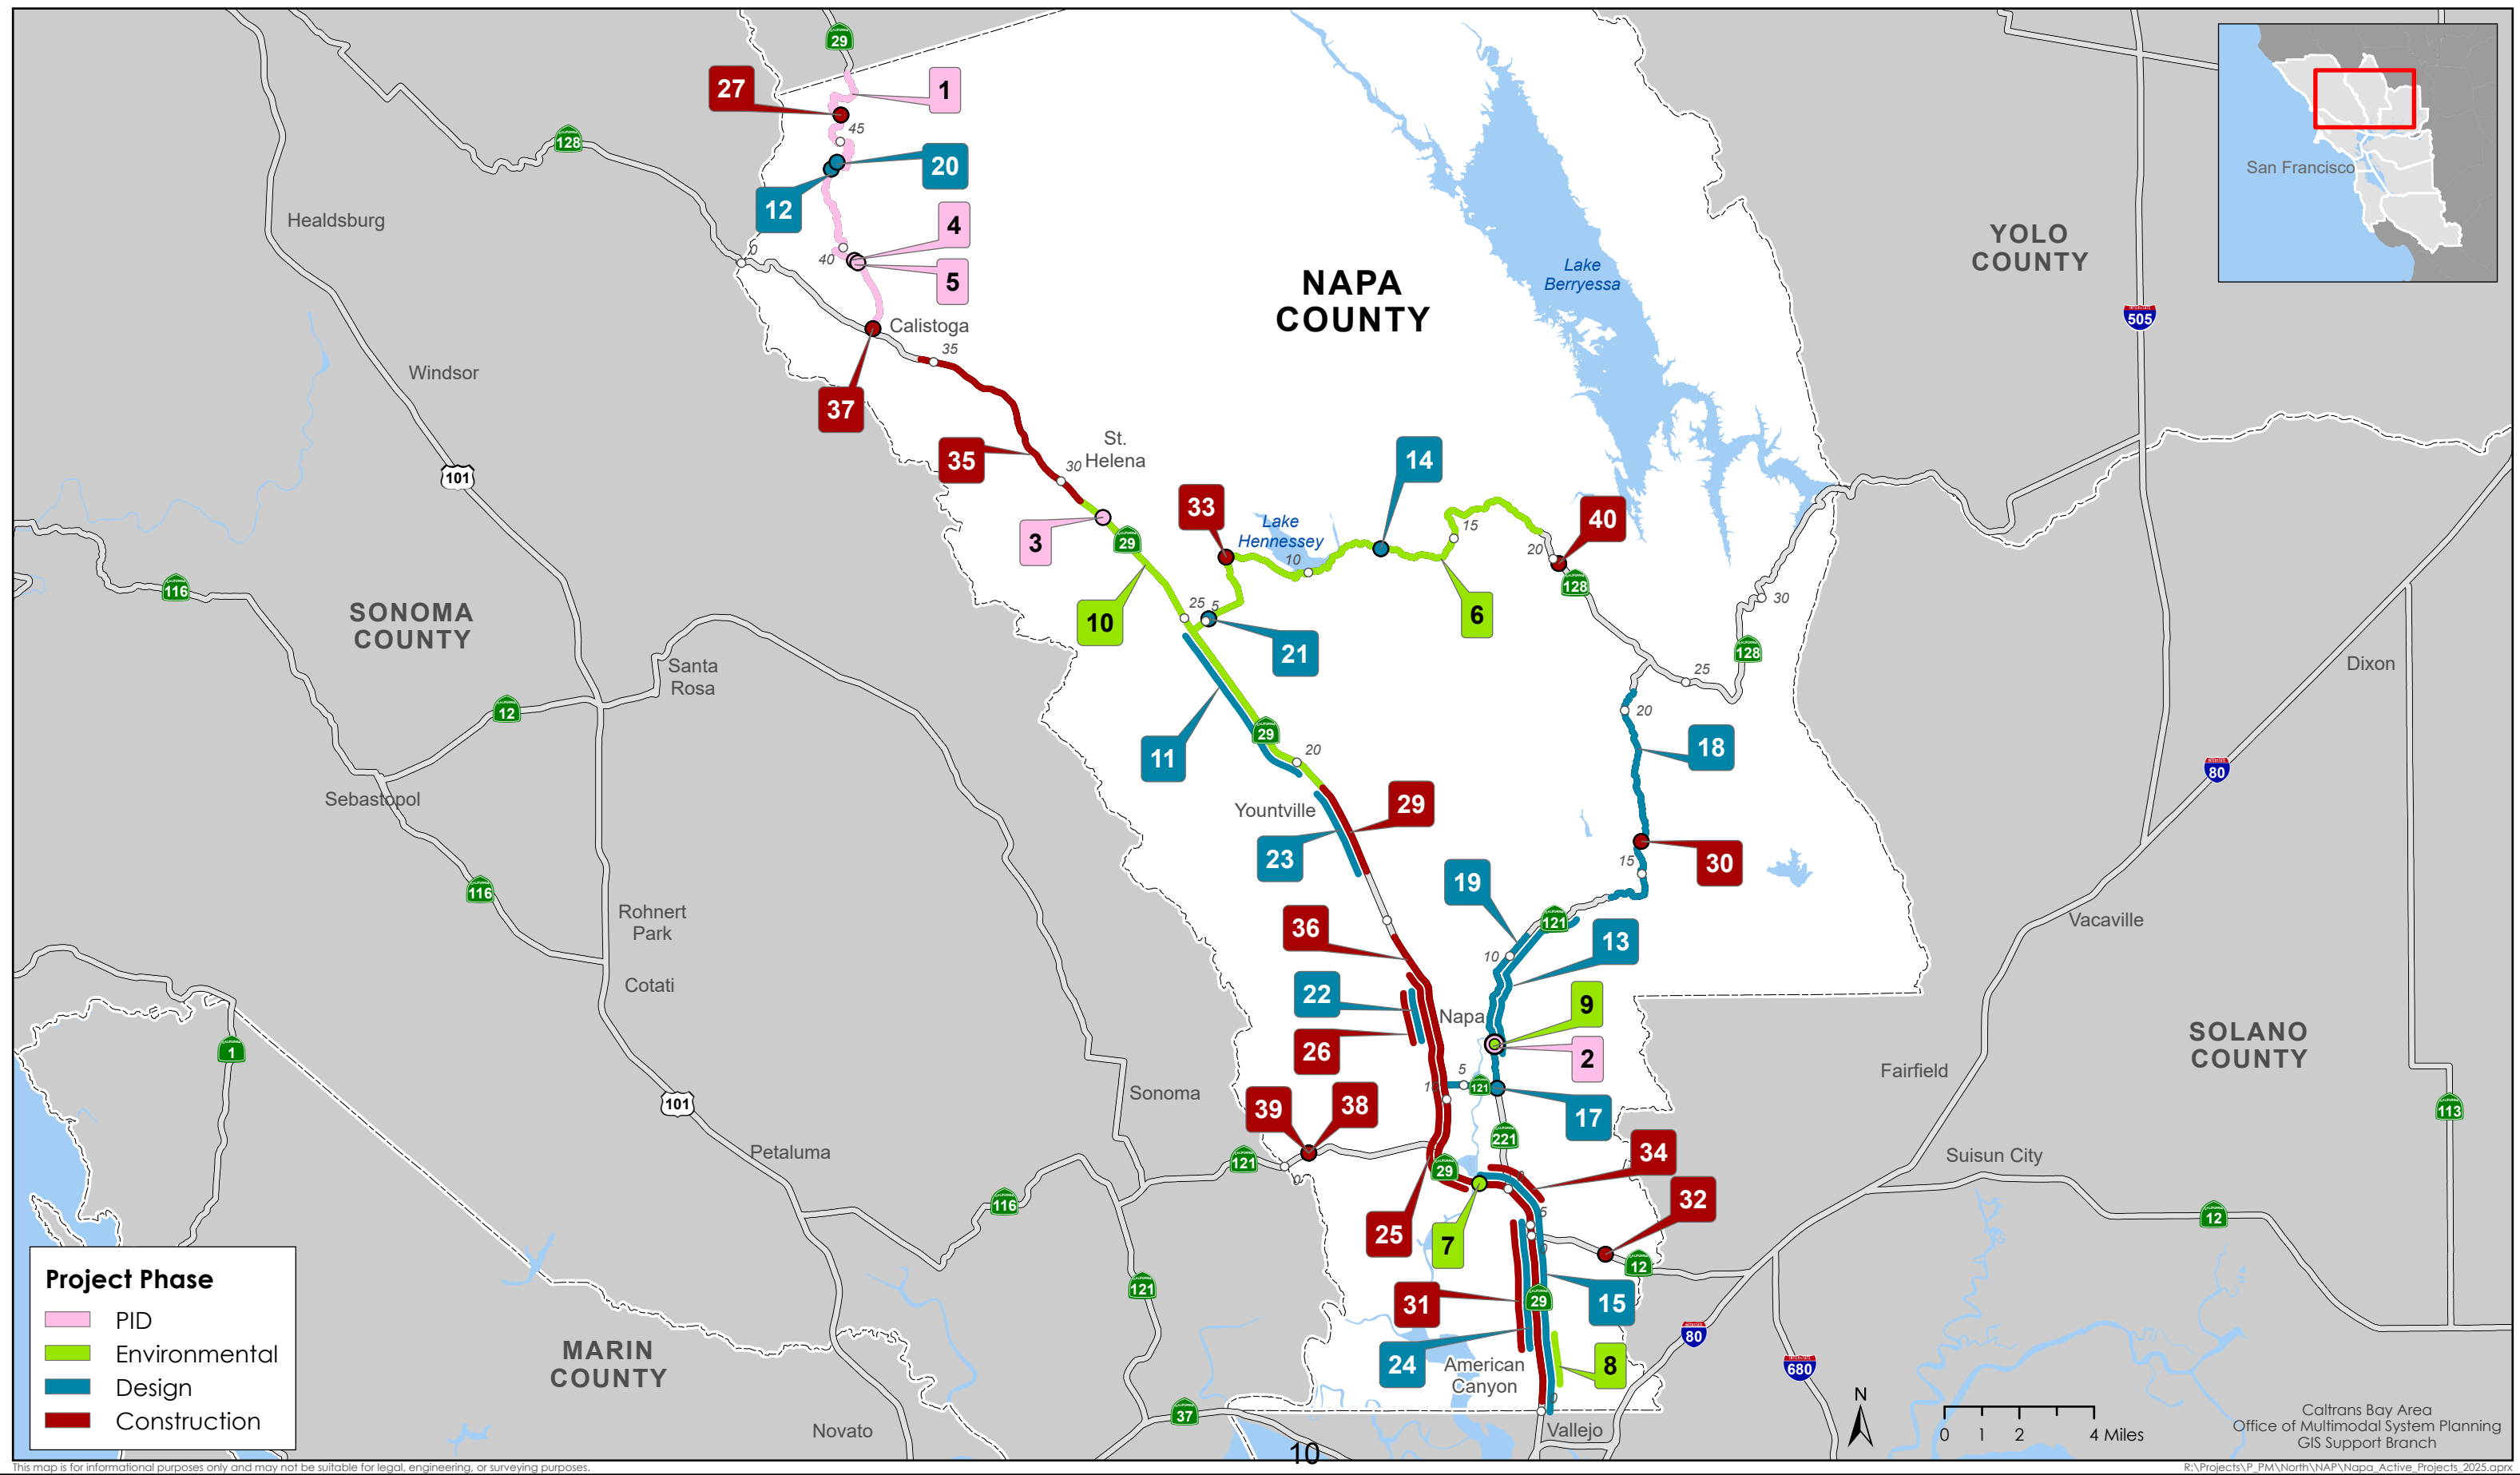

Caltrans District 4 Active Projects in Napa County- September 2025

MapID	Project Phase	EA	Rte	Postmile	Scope	Construction Capital	PAED	RTL	Construction Begin	Construction End
1	PID	2Q510	29	36.8/48.6	Pavement rehabilitation	TBD	TBD	05/2030	12/2030	05/2031
2	PID	4Y400	121	7.2/7.2	Intersection Improvement	TBD	TBD	TBD	TBD	TBD
3	PID	0W750	29	28.485/28.485	Intersection Improvement	TBD	TBD	TBD	TBD	TBD
4	PID	1X750	29	39.08	Garnett Creek Bridge Replacement	TBD	TBD	TBD	TBD	TBD
5	PID	1X760	29	38.96	Garnett Creek Branch Bridge Replacement	\$18.1M	10/2029	10/2032	04/2033	12/2034
6	Environmental	2W880	128	4.56/19.1	Napa City Pavement Preservation	\$13.8M	10/2026	05/2028	03/2029	11/2038
7	Environmental	4W370	29	6.99/6.99	Bridge Scour Mitigation	\$23.4M	10/2027	07/2029	01/2030	01/2031
8	Environmental	4Q010	29	0.69/R2.054	Multi-Modal Corridor Improvements	\$53.1M	07/2026	06/2028	01/2029	06/2030
9	Environmental	0J890	121	7.20/7.40	Intersection Improvement	\$18.0 M (\$1.0M SHOPP Contribution)	5/1/2026	4/30/2028	12/1/2028	12/2030
10	Environmental	0X110	29	19.00/29.25	Napa Valley Vine Trail gap closure project	\$25.3M	03/2026	11/2027	05/2028	07/2029
11	Design	2W430	29	19.70/24.60	Operational and Safety Improvements	\$8.55M	5/16/2025	07/2026	09/2026	08/2028
12	Design	2W370	29	42.57	Replace failed netting with new netting, remove debris, and install additional erosion control.	\$1.8M	4/28/2025	05/2026	02/2027	05/2028
13	Design	0Q800	121	6.9/12.1	Permanent Restoration; Inject grout at sinkhole and install drainage	\$997K	10/15/2024	04/2026	12/2026	12/2027
14	Design	4AA30	128	12.5	Storm Damage Restoration	\$5.3M	12/18/2024	10/2026	05/2027	06/2028
15	Design	4AC80	29	0.0/7.0	Pavement rehabilitation	\$18.9M	6/28/2024	06/2025	01/2026	01/2027
16 (Not mapped)	Design	4AC90	VAR	Var	Install/ Upgrade Horizontal Alignment Warning Signs	\$5.56M	6/21/2024	06/2025	12/2025	04/2028
17	Design	4J820	121	5.9	Bridge Replacement	\$15.6M	3/27/2023	08/2027	02/2028	12/2030
18	Design	0Q790	121	13.37/20.73	Construct RSP at five slipout locations.	\$4.3M	02/2023	08/2027	02/2028	12/2028
19	Design	1Q620	121	4.47/10.7	Pavement repair	\$35M	6/30/2022	08/2025	03/2026	06/2027
20	Design	2J88U	29	42.83	Sub-structure rehabilitation and-One Bridge scour mitigation	\$2.2M	2/1/2019	11/2025	04/2026	04/2028
21	Design	4J830	128	5.1	Bridge Replacement	\$12.2M	6/29/2022	08/2027	02/2028	12/2030
22	Design	0Q82A	29	11.6/13	Lincoln Ave Mitigation & Bio Monitoring	\$253K	N/A	12/2025	06/2026	09/2030
23	Design	0K63A	29	16.5/19.00	Plant Establishment and Environmental Mitigation	\$265K	N/A	4/21/2025	10/2025	06/2028
24	Design	4J411	29	1.7/5.1	Sheehy Xrk Plant Mitigation	\$910K	N/A	4/9/2025	09/2025	12/2035
25	Construction	2Q610	29	R7.3/13.5	Pavement rehabilitation.	\$23.3M	4/20/2022	5/3/2024	11/26/2024	11/2026
26	Construction	0Q820	29	11.6/13.0	Repair Culvert and stabilize the roadway.	\$24.47M	9/10/2021	12/4/2023	10/1/2024	12/2026
27	Construction	0Q830	29	46.1	Construct CIDH segmented pile wall at slipout	\$1.7M	6/29/2022	1/22/2024	7/12/2024	03/2026
28 (Not mapped)	Construction	3Q760	29	Var	Construct rumble strips at seven locations.	\$3.3M	12/31/2021	6/26/2023	3/27/2024	12/31/2024
29	Construction	0K630	29	16.48/19.04	Upgrade / Replace Bridge Rails	\$4.7M	10/22/2020	12/5/2022	7/14/2023	11/2025
30	Construction	0Q810	121	16.0/16.1	Repair pavement, replace drainage systems and upgrade guardrail.	\$1.3M	2/2/2022	12/2/2024	1/23/2024	12/2/2024
31	Construction	4J410	29	1.7/5.1	Rehabilitate Culverts	\$3.3M	02/2020	10/3/2022	4/7/2023	11/2025
32	Construction	0Q690	12	2.1/2.6	Construct Rock Slope Protection (RSP) to prevent further slope washout and pavement repair	\$1.2M	12/1/2020	6/24/2022	3/3/2023	10/30/2024

Caltrans District 4 Active Projects in Napa County- September 2025

MapID	Project Phase	EA	Rte	Postmile	Scope	Construction Capital	PAED	RTL	Construction Begin	Construction End
33	Construction	1G43A	128	R7.4	Environmental mitigation, monitoring and report at Conn Creek	\$0.2M	10/5/2015	8/23/2021	7/26/2022	10/2031
34	Construction	28120	29	5.45/R6.7	Construct New Interchange at SR 221/29/12	\$36.7M	2/13/2020	8/26/2021	5/13/2022	11/2026
35	Construction	2Q260	29	29.24/35.34	Vine Trail-Construct Class 1 Multiuse Path	\$13.2M	11/6/2020	12/10/2021	6/15/2022	4/1/2025
36	Construction	0K000	29	0.23/14.6	Upgrade Pedestrian Facilities	\$2.1M	7/1/2019	9/22/2021	4/8/2022	6/28/2024
37	Construction	3G64A	29	37.0	Environmental mitigation at Napa River Bridge	\$0.5M	2/9/2015	5/29/2019	5/28/2020	12/2028
38	Construction	4G210	121	0.75	Remove existing triple box culverts and replace with a new single span bridge	\$8.7M	4/9/2018	12/8/2020	6/10/2021	4/30/2024
39	Construction	4G21A	121	0.75	Environmental mitigation, monitoring and report at Huichica Creek	\$1M	4/9/2018	6/9/2023	12/20/2023	6/30/2033
40	Construction	4G84A	128	20.2	Environmental Permit Mitigation & Plant Establishment to Bridge Replacement	\$0.5M	6/16/2016	5/23/2022	12/21/2022	11/17/2031

PROJECT INITIATION REPORT

EA 4Y400

Operational Improvement; NAPA 121 PM 7.2 at Hennessy Drive in the City of Napa

Scope: Operational Improvement

EA 2Q510

Pavement Rehab; NAPA 29 PM 42.1/48.6 in County of Napa

Scope: Pavement rehabilitation and Safety Improvements

EA 0W750

Intersection Improvement; NAPA 29 PM 28.485 at Pope St. in the City of St. Helena

Scope: Intersection Improvement

EA 1X750

Garnett Creek Bridge Replacement; NAPA 29 PM 39.08 in the City of Calistoga

Scope: Bridge Replacement

EA 1X760

Garnett Creek Branch Bridge Replacement; NAPA 29 PM 38.96 in the City of Calistoga

Scope: Bridge Replacement

ENVIRONMENTAL

EA 2W880

Pavement Preservation; NAP 128 PM 4.56/19.10 in County of Napa from R29 to Knoxville Road

Scope: Pavement Preservation

Cost Estimate: \$13.8 M Construction Capital

Schedule: PAED: 10/2026 PS&E: 01/2028 RWC: 4/2028 RTL: 5/2028

EA 4W370

Bridge Scour Mitigation; NAPA 29 PM 6.99 in County of Napa at the Napa River BOH (aka George Butler Bridge)

Scope: Scour Mitigation, Seismic Retrofit, Bridge Rail upgrade. ~~for Class I Bike Path~~

Cost Estimate: \$14.6 M Construction Capital

Schedule: PAED: 10/2027 PS&E: 4/2029 RWC: 5/2029 RTL: 7/2029

EA 4Q010

NAPA 29 PM 0.6/R2.5 in City of American Canyon

Scope: Multi-Modal Corridor Improvements

Between Napa Junction Rd and American Canyon Rd

Cost Estimate: \$ 53.1 M Construction Capital

Schedule: PSR/PDS: 2/6/2023 PAED: 7/2026 PS&E: 12/2027 RWC: 6/2028 RTL: 6/2028

A PAED coop agreement is executed on 2/29/2024

PIR (Project Initiation Report)

PAED (Project Approval/ Environmental Document)

RWC (Right of Way Certification)

ADV (Advertise Contract)

PSR (Project Study Report)

RTL (Ready to List)

BO (Bid Open)

DED (Draft Environmental Document)

PSE (Plans, Specifications, and Estimate)

CCA (Construction Contract Acceptance)

AWD (Award Contract)

EA 0J890**5-Way Intersection; NAPA 121-PM 7.3 in City of Napa****Scope:** Intersection Improvement

At the intersection of Rt 121, Third St, East Ave and Coombsville

Cost Estimate: \$34.95 M Construction Capital (\$3.90 M SHOPP Contribution)**Schedule:** **DED:** 08/28/2025 **PAED:** 5/2026 **PS&E:** 4/2028 **RWC:** 4/2028**RTL:** 4/2028

A coop agreement is executed on 8/28/2023

EA 0X110**Napa Valley Vine Trail Gap Closure; NAPA 29 PM 19.00/29.25 in County of Napa****Scope:** Construct Class I & Class III Bicycle Facilities

From California Drive in the Town of Yountville to Pratt Ave

Cost Estimate: \$25.3 M Construction Capital**Schedule:** **DED:** 10/2025 **PAED:** 3/2026 **PS&E:** 2/2027 **RWC:** 9/2027 **RTL:** 11/2027**DESIGN****EA 2W370****Major Damage; NAPA 29 PM 42.57 in County of Napa****Scope:** Replace failed netting with new netting, remove debris, and install additional erosion control.**Cost Estimate:** \$1.8 M Construction Capital**Schedule:** **PAED:** 4/28/2025 **PS&E:** 3/2026 **RWC:** 4/2026 **RTL:** 5/2026**EA 4AA30****Storm Damage; NAPA 128 PM 12.5 in County of Napa****Scope:** Storm Damage Restoration – Install Soil Nail Wall**Cost Estimate:** \$5.3 M Construction Capital**Schedule:** **PAED:** 12/18/2024 **PS&E:** 08/2026 **RWC:** 9/2026 **RTL:** 10/2026**EA 0Q800****Major Damage; NAPA 121 PM 6.9/12.1 in County of Napa****Scope:** Permanent Restoration; Inject grout at sinkhole and install drainage**Cost Estimate:** 1 M Construction Capital**Schedule:** **PA&ED:** 10/2024 **PS&E:** 11/2025 **RWC:** 03/2026 **RTL:** 04/2026**EA 0Q82A****Mitigation & Bio Monitoring for Storm Damage; NAPA 29 PM 11.6/13.0 in County of Napa****Scope:** Environmental mitigation at Multiple Locations**Cost Estimate:** 253K Construction Capital**Schedule:** **PS&E:** 3/2026 **RWC:** 3/2026 **RTL:** 5/2026**PIR** (Project Initiation Report)**PAED** (Project Approval/ Environmental Document)**RWC** (Right of Way Certification)**ADV** (Advertise Contract)**PSR** (Project Study Report)**RTL** (Ready to List)**BO** (Bid Open)**DED** (Draft Environmental Document)**PSE** (Plans, Specifications, and Estimate)**CCA** (Construction Contract Acceptance)**AWD** (Award Contract)

EA 0Q79A**Mitigation & Bio Monitoring for Storm Damage; NAPA 121 PM 13.37/20.73 (5 locations) in County of Napa**

Scope: Construct RSP at five slip-out locations.

Cost Estimate: \$600 K Construction Capital

Schedule: PS&E: 8/2026 RWC: 12/2026 RTL: 12/2026

EA 4AC80**Pavement Rehab; NAPA 29 PM 0.0/7.0 in American Canyon & County of Napa**

Scope: Pavement rehabilitation

Cost Estimate: \$18.91 M Construction Capital

Schedule: PAED: 6/28/2024 PS&E: 9/2026 RWC: 10/2026 RTL: 11/2026

EA 4AC90**Safety; Various Locations in County of Napa**

Scope: Install/ Upgrade Horizontal Alignment Warning Signs

Cost Estimate: \$4.47 M Construction Capital

Schedule: PAED: 6/21/2024 PS&E: 6/2025 RWC: 6/2025 RTL: 6/2025

EA 4J820**Tulucay Creek Bridge Replacement; NAPA 121 PM 5.9 in City of Napa**

Scope: Bridge Replacement

Cost Estimate: \$15.6M Construction Capital

Schedule: DED: 06/30/2022 PAED: 03/27/2023 PS&E: 05/2027 RWC: 07/2027 RTL: 08/2027

EA 0Q790**Storm Damage; NAPA 121 PM 13.37/20.73 (5 locations) in County of Napa**

Scope: Construct RSP at five slip-out locations.

Cost Estimate: \$2.4 M Construction Capital

Schedule: PAED: 02/9/2023 PS&E: 04/16/2025 RWC: 04/24/2025 RTL: 05/05/2025

EA 1Q620**Pavement Rehab; NAPA 121 PM 4.47/10.7 in City of Napa**

Scope: Pavement repair.

Cost Estimate: \$39.6 M Construction Capital

Schedule: PAED: 06/30/2022 PS&E: 06/2027 RWC: 08/2027 RTL: 08/2027

EA 2J88U**No-Name Creek Bridge: NAPA 29-PM 42.83 in County of Napa**

Scope: Sub-structure rehabilitation and scour mitigation at one bridge

Cost Estimate: \$2.20M Construction Capital

Schedule: PAED: 2/1/2019 PS&E: 10/2025 RWC: 10/2025 RTL: 11/2025

PIR (Project Initiation Report)

PAED (Project Approval/ Environmental Document)

RWC (Right of Way Certification)

ADV (Advertise Contract)

PSR (Project Study Report)

RTL (Ready to List)

BO (Bid Open)

DED (Draft Environmental Document)

PSE (Plans, Specifications, and Estimate)

CCA (Construction Contract Acceptance)

AWD (Award Contract)

NVTA - Caltrans Report

EA 4J990**Storm Water Quality Improvement; NAPA 29 PM 33.13 in County of Napa**

Scope: Improve water quality and fish passage

Cost Estimate: \$6.9M Construction Capital

Schedule: DED: 12/2/2020 PAED: 06/30/2021 PS&E: TBD RWC: TBD RTL: TBD

EA 4J830**Hopper Slough Creek; NAPA 128 PM 5.1 in County of Napa**

Scope: Bridge Replacement

Cost Estimate: 12.2 M Construction Capital

Schedule: DED: 03/18/2022 PAED: 06/29/2022 PS&E: 05/2027 RWC: 07/2027 RTL: 08/2027

EA2W430**Napa Forward Intersection Improvements; NAPA 29 PM 22.72 in County of Napa**

Scope: Operational and Safety Improvements at the intersection of Oakville Cross Rd and Rutherford Rd

Cost Estimate: \$8.5 M Construction Capital

Schedule: DED: 01/31/2024 PAED: 05/16/2025 PS&E: 06/2026 RWC: 07/2026 RTL: 07/2026

EA4J411**Revegetation mitigation and monitoring; NAPA 29 PM 1.7/PM 5.1 in American Canyon**

Scope: Plant establishment and monitoring work for drainage improvement EA 4J410 at Rio Del Mar

Cost Estimate: \$0.91 M Construction Capital

Schedule: PS&E: 02/4/2025 RWC: 02/11/2025 RTL: 04/9/2025

EA0K63A**Plant Establishment and Environmental Mitigation; NAPA 29 PM 1.7/PM 5.1 in County of Napa**

Scope: Plant establishment and environmental mitigation and monitoring work for bridge rail upgrade EA 0K630 In and near Yountville, at Dry Creek Bridge, Perfume Creek Bridge and California Drive UC.

Cost Estimate: \$0.31 M Construction Capital

Schedule: PS&E: 03/18/2025 RWC: 04/02/2025 RTL: 04/21/2025

CONSTRUCTION**EA 2Q610****Pavement Rehab; NAPA 29 PM R7.3/13.5 in County of Napa**

Scope: Pavement rehabilitation.

Cost Estimate: \$23.3M Construction Capital

Schedule: PAED: 04/20/2022 PS&E: 04/2024 RWC: 04/2024 RTL: 05/2024 AC: 11/27/2024 CCA: 11/2026

Awarded Contractor: Granite Rock Company

PIR (Project Initiation Report)

PAED (Project Approval/ Environmental Document)

RWC (Right of Way Certification)

ADV (Advertise Contract)

PSR (Project Study Report)

RTL (Ready to List)

BO (Bid Open)

DED (Draft Environmental Document)

PSE (Plans, Specifications, and Estimate)

CCA (Construction Contract Acceptance)

AWD (Award Contract)

NVTA - Caltrans Report

EA 0Q820**Storm Damage; NAPA 29 PM 11.6/13.0 in City of Napa****Scope:** Repair Culvert and stabilize the roadway at Lincoln Ave**Cost Estimate:** \$24.475M Construction Capital**Schedule:** PAED: 09/10/2021 PS&E: 11/2023 RWC: 11/2023 RTL: 12/2023 AC: 10/2024 CCA: 12/2026**EA 0Q830****Storm Damage; NAPA 29 PM 46.1 in County of Napa****Scope:** Construct CIDH segmented pile wall at slip out**Cost Estimate:** \$1.7M Construction Capital**Schedule:** PAED: 06/29/2022 PS&E: 1/11/2024 RWC: 1/11/2024 RTL: 1/22/2024 AC: 07/12/2024 CCA: 03/2026**EA 3Q760****Rumble Strips; NAPA 29, 121 & 128 Various Locations in County of Napa****Scope:** Construct rumble strips at seven locations.**Cost Estimate:** \$3.3M Construction Capital**Schedule:** PAED: 12/31/2021 RTL: 6/26/2023 AWD: 2/29/2024 AC: 03/27/2024 CCA: 12/31/2024 EP: 12/2025**EA 0K630****Bridge Rails; NAPA 29 PM 16.48/19.04 in County of Napa****Scope:** Upgrade / Replace Bridge Rails in 3 Bridges**Cost Estimate:** \$4.7M Construction Capital**Schedule:** PAED: 10/22/2020 PS&E: 12/02/2022 RWC: 12/05/2022 RTL: 12/05/2022 AC: 07/14/2023 CCA: 11/2025**EA 0Q810****Storm Damage; NAPA 121 PM 16.0/16.1 in County of Napa****Scope:** Repair pavement, replace drainage systems and upgrade guardrail.**Cost Estimate:** \$1.3M Construction Capital**Schedule:** PAED: 02/02/2022 RTL: 06/26/2023 AWD: 12/29/2023 AC: 1/23/2024 CCA: 12/2/2024 EP: 12/2025**Awarded Contractor:** Argonaut Constructors**EA 4J410****Drainage Improvement; NAPA 29 PM 1.7/5.1 in City of American Canyon****Scope:** Rehabilitate Culverts**Cost Estimate:** \$3.3M Construction Capital**Schedule:** PAED: 2/4/2020 RTL: 10/3/2022 AWD: 3/21/2023 AC: 04/07/2023 CCA: 11/2025**Awarded Contractor:** Terracon Constructors Inc.**EA 0Q690****Storm Damage; NAPA 12 PM 2.1/2.6 in County of Napa****Scope:** Construct Rock Slope Protection (RSP) to prevent further slope washout and pavement repair**Cost Estimate:** \$1.2M Construction Capital**Schedule:** PAED: 12/1/2020 RTL: 06/24/2022 AWD: 3/21/2023 AC: 03/03/2023 CCA: 10/30/2024 EP: 12/2026**PIR** (Project Initiation Report)**PAED** (Project Approval/ Environmental Document)**RWC** (Right of Way Certification)**ADV** (Advertise Contract)**PSR** (Project Study Report)**RTL** (Ready to List)**BO** (Bid Open)**DED** (Draft Environmental Document)**PSE** (Plans, Specifications, and Estimate)**CCA** (Construction Contract Acceptance)**AWD** (Award Contract)

EA 1G43A**Env. Mitigation at Conn Creek; NAPA 128 PM R7.4 on Silverado Trail in County of Napa****Scope:** Environmental mitigation, monitoring and report at Conn Creek**Cost Estimate:** \$0.2M Construction Capital**Schedule:** PAED: 10/5/2015 PS&E: 6/28/2021 RWC: 08/10/2021 RTL: 08/23/2021 AC: 07/26/2022 CCA: 10/2031**EA 28120****Soscol Junction Improvement; NAPA 29 PM 5.0/7.1 and NAPA 221 PM 0.0/0.7 in County of Napa****Scope:** Construct New Interchange at SR 221/29/12**Cost Estimate:** \$36.7M Construction Capital**Schedule:** PAED: 2/13/2020 PSE: 08/26/2021 RWC: 08/25/2021 RTL: 08/26/21 AC: 05/13/2022 CCA: 11/2026**EA 2Q260****Napa Valley Vine Trail; NAPA 29-PM 33.4/37.9 in County of Napa****Scope:** Construct Class 1 Multiuse Path**Cost Estimate:** \$13.2M Construction Capital**Schedule:** DED: 6/17/2020 PAED: 01/15/2021 PS&E: 12/10/2021 RWC: 12/10/2021 RTL: 12/10/2021**AWD:** 5/20/2022 (Ghilotti Construction Company) **AC:** 06/15/2022 **CCA:** 09/2025**EA 3G64A****Env. Mitigation & Plant Establishment at Napa River Bridge; NAPA 29 PM 37.0 in City of Calistoga****Scope:** Environmental mitigation at Napa River Bridge**Cost Estimate:** \$0.5M Construction Capital**Schedule:** PAED: 2/9/2015 RTL: 5/29/2019 AWD: 3/26/2020 (Hanford Applied) AC: 05/28/2020 CCA: 12/2028**EA 4G210****Widen Roadway at Huichica Creek; NAPA 121-PM 0.75 in County of Napa****Scope:** Remove existing triple box culverts and replace with a new single span bridge**Cost Estimate:** \$8.7M Construction Capital**Schedule:** PAED: 4/9/2018 RTL: 12/8/2020 AWD: 5/19/2021 (Gordon Ball Inc) CCA: 04/30/2024 EP: 9/2026**EA 4G21A****Env. Mitigation at Huichica Creek; NAPA 121-PM 0.75 in County of Napa****Scope:** Environmental mitigation, monitoring and report at Huichica Creek**Cost Estimate:** \$1.0M Construction Capital**Schedule:** PAED: 4/9/2018 RTL: 06/9/2023 AWD: 11/28/2023 AC: 12/20/2023 CCA: 06/2033**EA 4G84A****Capell Creek Bridge Env Mitigation; NAPA 128-PM 20.2 in County of Napa****Scope:** Environmental Permit Mitigation & Plant Establishment to Bridge Replacement**Cost Estimate:** \$0.5M Construction Capital**Schedule:** PAED: 6/16/2016 RTL: 05/23/2022 AWD: 11/17/2022 CCA: 11/2031**PIR** (Project Initiation Report)**PAED** (Project Approval/ Environmental Document)**RWC** (Right of Way Certification)**ADV** (Advertise Contract)**PSR** (Project Study Report)**RTL** (Ready to List)**BO** (Bid Open)**DED** (Draft Environmental Document)**PSE** (Plans, Specifications, and Estimate)**CCA** (Construction Contract Acceptance)**AWD** (Award Contract)

EA 0K000

ADA Compliance; NAPA 29 PM 0.23/14.6 in County of Napa

Scope: Upgrade Pedestrian Facilities

Cost Estimate: \$2.1M Construction Capital

Schedule: **PAED:** 7/1/2019 **RTL:** 09/22/2021 **AWD:** 03/17/2022 **AC:** 04/08/2022 **CCA:** 6/28/2024 **EP:** 04/01/2025

ACTION ITEMS

PIR (Project Initiation Report)	PSR (Project Study Report)	DED (Draft Environmental Document)
PAED (Project Approval/ Environmental Document)		PSE (Plans, Specifications, and Estimate)
RWC (Right of Way Certification)	RTL (Ready to List)	CCA (Construction Contract Acceptance)
ADV (Advertise Contract)	BO (Bid Open)	AWD (Award Contract)
